Department of Social Welfare and Development
Field Office Caraga
DISASTER RESPONSE MANAGEMENT DIVISION

OWD - 01-1054

Risk Resiliency Program through Cash-for-Training and Work

Project LAWA at BINHI

(Local Adaptation to Water Access and Breaking Insufficiency through Natural Harvest for the Impoverished)

REGIONAL PROGRAM IMPLEMENTATION PLAN
C.Y. 2025

Phases	Activities	Timeframe
Pre implementation Phase	Staff meeting for 2025 updates and directives	Jan. 6-10, 2025
	Preparation of RSO and introductory letter for field-based staff	Jan. 6-10, 2025
	Preparation of Monthly Work and Travel Plan for the month of January	Jan. 6-10, 2025
	Staff deployment, courtesy call and coordination with LGUs' LCEs and TWG members	Jan. 13-17, 2025
	Preparation and sending of invitation for TWG Forum cum Regional Strategic Planning Workshop	Jan. 13-17, 2025
	Release of funds by DRMB-CO to DSWD FOs	Jan. 20-24, 2025
	MTWG coordination meeting and conduct of MLGU Forum	Jan. 20-24, 2025
	Issuance and submission of EO for TWG by LGU	Jan. 20-31, 2025
	Lobbying, forging and submission of MOA with FO and LGUs	Jan. 20 - Feb. 14, 2025
	Project site validation	Jan. 20-31, 2025
	Geotagging of project sites (before implementation)	Jan. 20-31, 2025
	Preparation of project proposal and breakdown of allocation	Jan. 20-31, 2025
	Provision of technical assistance in the preparation and finalization of project proposal and breakdown of allocation by FO to LGUs	Jan. 20-31, 2025
	Preparation and submission of any binding agreement for lot utilization (e.g. usufruct, MOA, resolution)	Jan. 20 - Feb. 14, 2025
	Preparation and approval of masterlist of eligible beneficiaries by LGU	Jan. 27 - Feb. 21, 2025
	Administration of FACED by LGU	Jan. 27 - Feb. 21, 2025
	Facilitate approval of project proposal and breakdown of allocation by LGU and FO and submission to DRMB-Central Office	Feb. 1-7, 2025
	Consultation and cascading of guidance by FO to LGUs and other stakeholders (TWG Forum)	Feb. 10-12, 2025
	Accomplishment of baseline data by LGU and FO through MER tool	Feb. 10-14, 2025
	Planning and harmonization of FO and LGU activities (Planning Workshop with RRP)	Feb. 20-21, 2025
	Pre-Implementation Meeting and Orientation with Municipal and Barangay LGUs	Feb. 24-28, 2025
Implementation Phase	**Cash-for-Training (Stage-1) - Advance Climate Action**	
	A. Discussion on Project LAWA and BINHI Modules	Mar. 3 - Apr. 30, 2025
	B. Discussion on DSWD protection laws, health and safety protocols	
	C. Discussion on LAWA at BINHI implementation and management	
	Cash-for-Work (Stage-2) - Project Implementation	
	A. Actual conduct of the activities (CFW)	Mar. 6 - May. 16, 2025
	B. Monitoring in the conduct of activities (CFW)	
	C. Geotagging of project sites (during and after CFW)	
	Cash-for-Training (Stage-3) - Sustainability Programming	
	A. Sustainability Training	

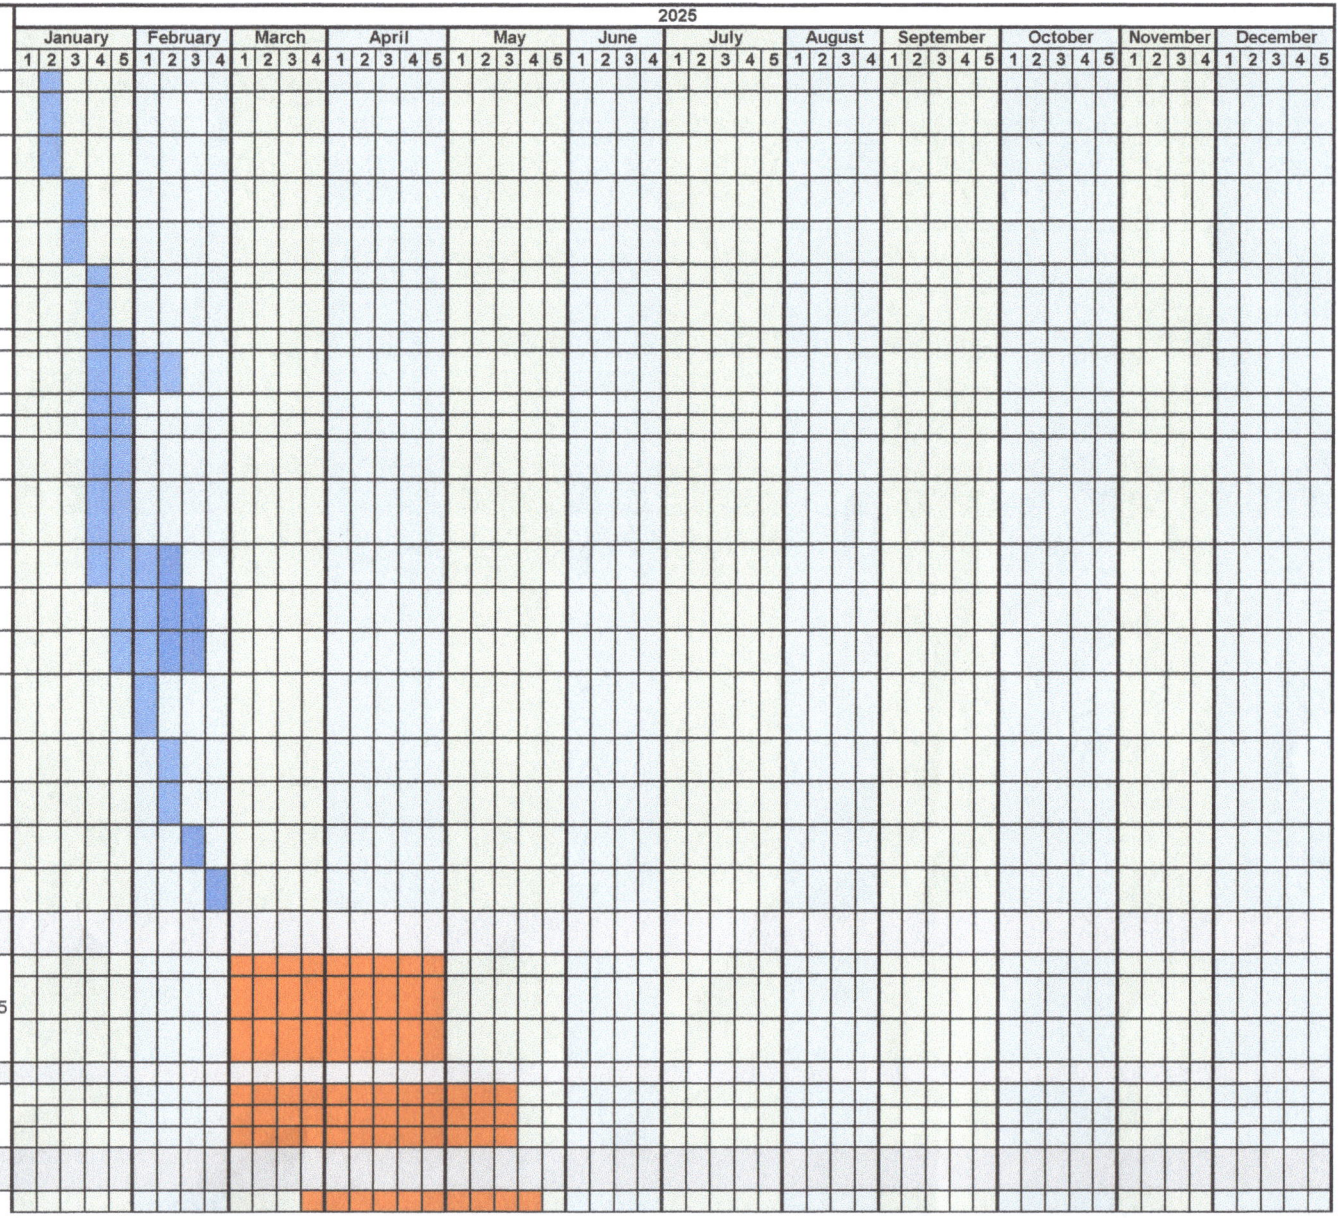

Phases	Activities	Timeframe
	A. Sustainability Training	Mar. 24 - May. 20, 2025
	B. Assessment and Formulation of Community Action Plan (CAP)	
	C. Turn over Ceremony	
	Review and submission of post-implementation documents	Mar. 25 - May. 30, 2025
	Conduct of payout	Apr. 16 - Jun. 16, 2025
Post Implementation Phase	Liquidation	Apr. 28 - Jul. 15, 2025
	Generation and updating of reports by PDOs re: Project Implementation	Apr. 1 - Jul. 31, 2025
	Submission of monthly, quarterly, semestral and annual reports to Central Office	Apr. 10 - Dec. 31, 2025
	Post-implementation Monitoring	Aug. 1-31, 2025
	Documentation of good practices, challenges and recommendations	Aug. 1-31, 2025
	Monitoring and Technical Assistance (MATA) by DRMB-Central Office	Sep. 1-15, 2025
	Experiential Learning Exchange with other FOs	Sep. 16-30, 2025
	Participation/Attendance to Capacity-Building Activities of DRMD	Oct. 1- Nov. 30, 2025
	Program Implementation Review with LGUs and partners	Nov. 1-15, 2025
	Program implementation Review, Evaluation and Planning Workshop with DRMB-CO	Nov. 16-30, 2025
Preparation for CY 2026 Program Implementation	Coordination with the LGUs and other stakeholders relative to the CY 2026 budget preparation	Sep. 1-15, 2025
	Project Site Validation for 2026 implementation	Sep. 16-30, 2025
	Preparation and Submission of Project Proposal and Breakdown of Allocation by LGU and Lobbying of MOA for CY 2026 Program Implementation	Oct. 1- 30, 2025
	Approval of Project Proposal and Breakdown of Allocation for CY 2026 Program Implementation	Dec. 1-31, 2025
	Planning Workshop for CY 2026 Program Implementation	Dec. 1-31, 2025
All Phases	Coordination with the LGUs and other stakeholders (meetings, documentation, etc.)	Pre Implementatiom - Jan 6 - Feb 28, 2025 Implementation - March 3 - July 31, 2025 Post implementation - August 1 - November 30, 2025 Preparation for 2026 - September 1 - December 31, 2025
	Conduct/Attendance to Bi-monthly Staff meeting	February 28, 2025 | April 25, 2025 | June 27, 2025 | August 29, 2025 | October 31, 2025 | December 12, 2025

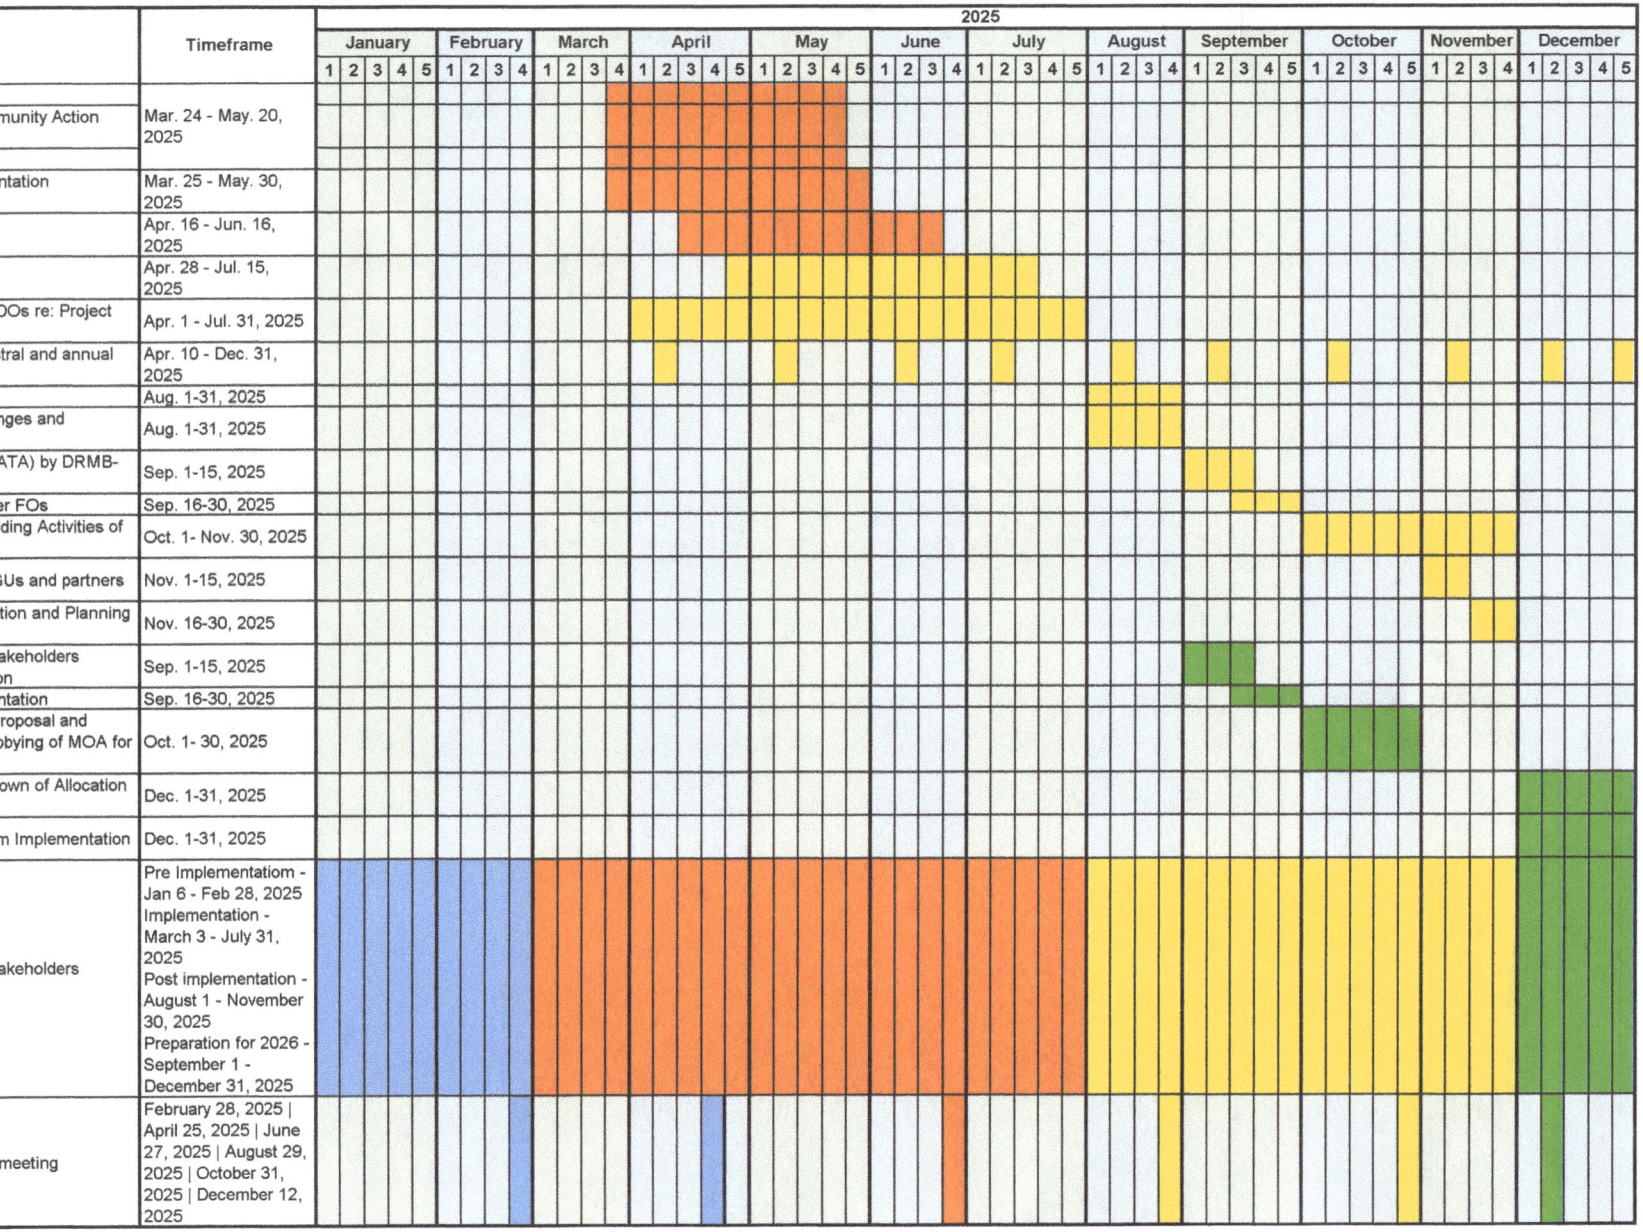

Legend: Pre-implementation Phase; Post-implementation Phase; Implementation Phase; Preparation for CY 2026 Program Implementation

Prepared by:

ALICIA T. MARQUISO
RRP Focal / Concurrent DRRS Head

Recommending Approval :

ALDIE MAE A. ANDOY
OIC-Chief, DRMD

Approved by :

MARLFLOR DOLLAGA - LIBANG
Regional Director

For the Regional Director:

TRISTAN C. TELEN, PhD. MA, REB
Director III / ARDA
